

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	19 September 2026
Team ID	Shaik Irshad - 238W1A4256
Project Name	Automated Network Request Management In ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The product backlog below breaks the Network Request solution's functional epics into estimated user stories, sequenced across two sprints. All fourteen stories were delivered by the solo project team member.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Network Request Submission	USN-1	As a requester, I can open the Network Request catalog item from the Service Portal and enter my request details.	2	High	Shaik Irshad
Sprint-1		USN-2	As a requester, I cannot submit the request if a mandatory field is left blank.	1	High	Shaik Irshad
Sprint-1		USN-3	As a requester, I can select whether my connection is New or Existing.	1	High	Shaik Irshad
Sprint-1	Dynamic Form Behaviour	USN-4	As a requester, I only see the “Enter your Existing ID” field when I select Existing connection.	2	Medium	Shaik Irshad
Sprint-1	Requester Info Auto-Population	USN-5	As a requester, my email, name and phone number are filled in automatically once I set “Opened on behalf of”.	2	Medium	Shaik Irshad
Sprint-1	Backend Configuration	USN-11	As an admin, I can see all submitted network requests as structured records in one custom table.	3	Medium	Shaik Irshad
Sprint-2	Email Notification	USN-6	As a requester, I receive an email once my request has been created in the backend.	2	High	Shaik Irshad
Sprint-2	Status Tracking & Traceability	USN-7	As a requester, I can check whether my request is still pending or has been Approved/Rejected.	2	High	Shaik Irshad
Sprint-2	Approval Workflow	USN-8	As an approver, I receive an approval request when a new Network Request is submitted.	1	High	Shaik Irshad
Sprint-2		USN-9	As an approver, I can approve or reject a network request.	2	High	Shaik Irshad
Sprint-2		USN-10	As an approver, my decision automatically updates the request's final status.	1	High	Shaik Irshad
Sprint-2	Backend Configuration	USN-12	As an admin, I can trace an approval back to the request record it belongs to.	2	Medium	Shaik Irshad
Sprint-2	Security & Access	USN-13	As an admin, I want the new table to be secured without building a custom access framework.	1	Low	Shaik Irshad
Sprint-2	Troubleshooting	USN-14	As an admin, I can diagnose why a submission did not trigger the expected automation.	2	Medium	Shaik Irshad

Sprint Schedule:

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	11	6 Days	01 Aug 2026	06 Aug 2026	11	06 Aug 2026
Sprint-2	13	6 Days	08 Aug 2026	13 Aug 2026	13	13 Aug 2026

Project Tracker, Velocity & Burndown Chart (4 Marks)


Velocity:

With a 6-day sprint duration and a combined velocity of 24 story points across the two sprints (12 days total), the team's average velocity (AV) per iteration unit (story points per day) is calculated as:


$$AV = \frac{\text{Velocity}}{\text{Sprint Duration}} = \frac{24}{12} = 2 \text{ story points/day}$$

Burndown Chart:

A burndown chart plots work remaining against time. The two charts below track story points remaining, day by day, against the ideal straight-line pace for each of the project's sprints. Both sprints finished on schedule, with the team running slightly ahead of the ideal pace through the middle of each sprint.

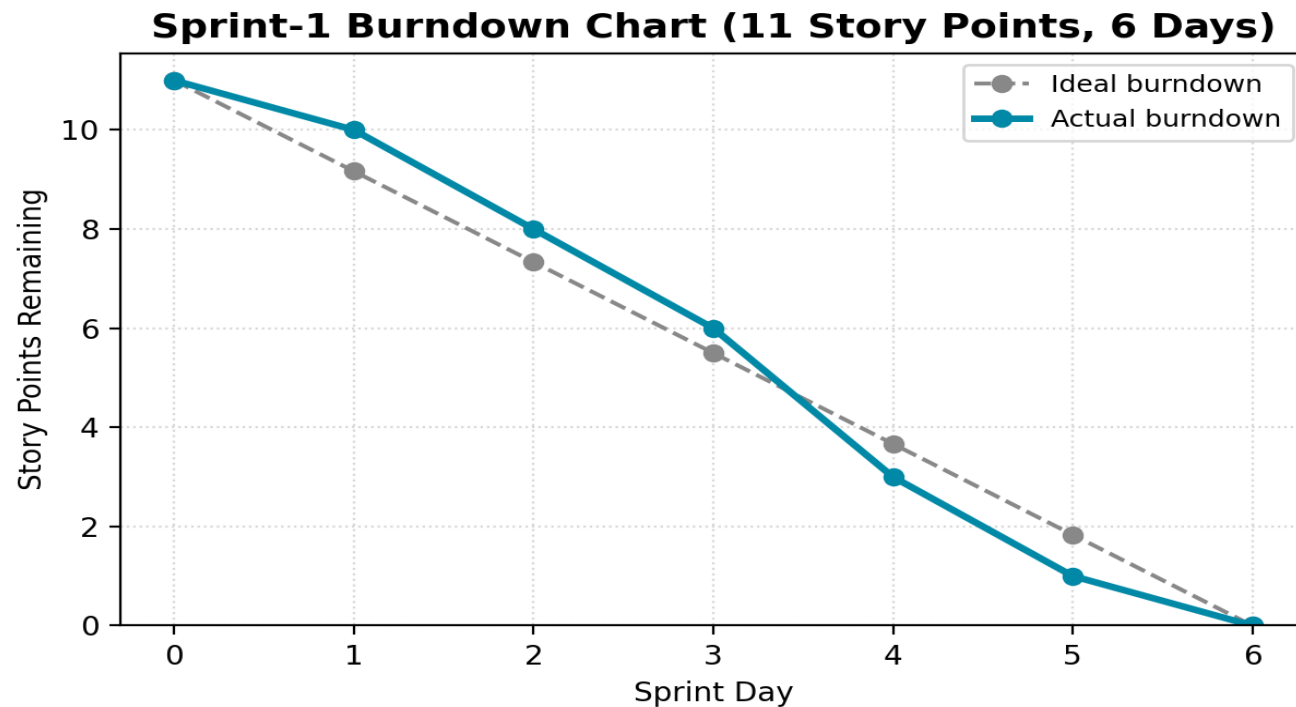

Sprint-2 Burndown Chart (13 Story Points, 6 Days)

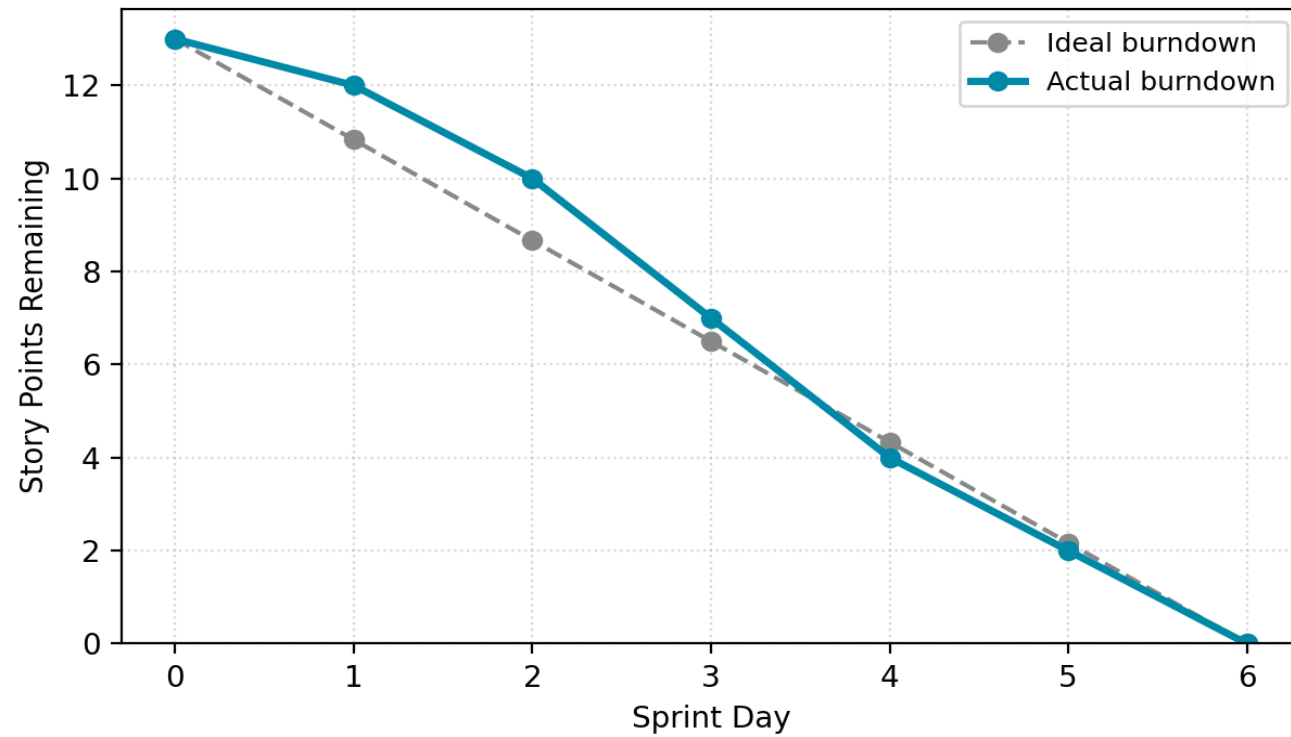

References:

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
